
Q2 — Building Mira (write-up)

Author: Srinivas Annam · **Stack:** n8n Cloud · OpenAI gpt-4o-mini · Langfuse (OpenTelemetry) · **Full detail:** PRD, workflow, evaluation, cost

Design and architecture

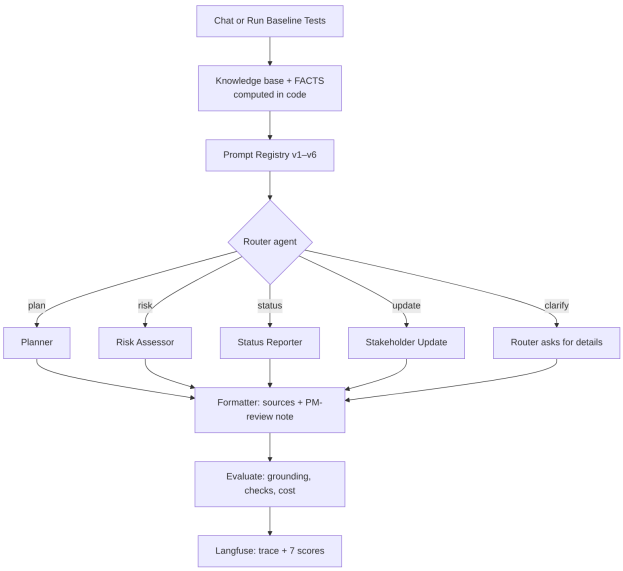

Orchestration: Router / Dispatcher. PM requests are one of four kinds (plan, risk, status, stakeholder update), and each needs different data. A router sends each request to one specialist:

- **Lower cost than a sequential pipeline:** a clarify answer costs $0.00019, a full plan $0.00077.
- **Easy to trace:** two LLM calls per request, router then specialist.
- **One agent per pain point**, each with its own prompt.

The rejected options:

- **Sequential pipeline:** runs every agent on every request, so it wastes cost.
- **Hierarchical:** only needed for multi-part requests (E10), and is next on the roadmap.

Agents and grounding. Each agent sees only its own slice of the data:

- **Planner:** description and timeline.
- **Risk Assessor:** risk register, plus a ranking of risks by live task evidence.
- **Status Reporter:** task board, timeline and per-sprint facts.
- **Stakeholder Update:** goals and per-sprint view.

Counts, overdue and due-soon tasks, health, milestone dates and risk ranking are **computed in JavaScript, not by the LLM**. The prompts tell the model to use those facts as given.

Human review. Every answer ends with its sources and "Draft for PM review", and nothing is sent automatically.

Tool choices

Need	Choice	Why
Workflow platform	n8n Cloud	Low-code, visual, exportable JSON; Code nodes for deterministic facts
LLM	gpt-4o-mini	~$0.00066 per request; JSON mode for the router; good enough once facts come from code
LLM calls	HTTP Request nodes (not the AI Agent node)	Returns token usage for cost tracking; no tools needed
Observability	Langfuse (US region, OpenTelemetry)	One trace per request with router and specialist generations, tokens, cost, latency and 7 scores
Evaluation	Ground-truth JSON + one check engine in JS (n8n) and Python (`score.py`)	The same checks run inside the live workflow and offline

Implementation

Capability	Status	Evidence (live, v6)
Project plan (core)	✅	T1: 8 named phases, dates, milestones; goals quoted exactly
Risk assessment (core)	✅	T3: all 10 register risks categorized with mitigations; T7: top 3 by evidence (R09, R01, R05)
Weekly status report (core)	✅	T5: Sprint 3 only, real task names, Phase 2 milestone; T8: T024 blocked, T006 overdue
Stakeholder Update Generator (extended)	✅	T12 leadership email (Sprint 2 only); E9 client email without owner names
Vague-input handling	✅	T2, T4, T6, T9 ask for scope, goals, timeline and team; no invented plan
Observability	✅	Every request traced in Langfuse; scores: id_grounding, footer, cost, latency, baseline_pass, check_rate, route_correct
Baseline dataset	✅	All 12 inputs + 11 edge cases, 151 checks; results in `results/`

Cost and evaluation

Cost per request (measured over 3 runs, gpt-4o-mini list prices):

Request	Cost	Latency
Project plan	**$0.00077**	10.5 s
Risk assessment	$0.00097	12.8 s
Sprint status report	$0.00106	8.5 s
Stakeholder email	$0.00063	3.9 s
Clarifying question	$0.00019	1.8 s
Average, all 69	**$0.00066**	4.4 s (median 3.2 s)

At 100 requests per PM per month, that is about $0.07 per PM, far below the $5 target. The 23-test suite costs $0.015 to run.

Metrics (definitions in 04-metrics.md):

Metric	Target	v1 naive	v3	v6 (3 runs)
Baseline pass rate (T1–T12)	≥ 11/12	7/12	12/12	**36/36**
All-tests pass rate	—	52%	96%	**69/69 (100%)**
Routing accuracy	≥ 95%	78%	100%	**100%**
Fabricated IDs	0	0	0	**0**
Cost per request	< $0.01	$0.00067	$0.00062	**$0.00066**

Observations

1. **Facts computed in code prevent fabricated data.** Even naive v1 prompts never invented an ID. But only prompt boundaries stopped the misuse of real data: v1 adopted a user's 30% goal and put owner names in a client email.
2. **The router can't see the data, so it must be told the data exists.** v2 over-asked for clarification on 6 answerable status questions. The v3 router prompt fixed this: routing went from 74% to 100%.
3. **Passing checks can hide wrong answers.** Reading every answer found T10 missing the Blocked count and T5 mixing project and sprint health. The checks were tightened. T5 was fixed only once per-sprint facts were computed in code; the prompt alone was not enough.
4. **One run is not enough.** Three runs of v5 showed T1 dropping phase names 1 time in 3. A one-line rule (v6) fixed it, and v6 passed 69/69.
